



See the latest construction progress on [webcam 1](#) and [webcam 2](#).

Upcoming and ongoing activity: How you may be affected

Area	Impact	Timing
Main Construction Site Internal (STKB)	Commissioning of mechanical and fire services approaches completion.	March/April
Main Construction Site External (STKB)	Flowerbeds and bridges being constructed. Paving works are proceeding.	March/April
Mary Glowrey Building (MGB) services upgrade	Mechanical and fire integration testing between the MGB & STKB approaches completion.	March/April
MGB Façade	Northern Fire Escape Stair – scaffold has been erected and façade treatment works are progressing. Landscaping and pathways to Victoria Parade frontage are being constructed. Façade will then be painted.	March/April
Civil Works	Half of Victoria Parade footpath has been laid with the rest planned for completion in late April. Napier Street reconstruction has begun and will be completed in April.	March/April
MGB Interconnections	Final touches are being made where doors that link the STKB and MGB are installed.	April
Main Construction Site	Pedestrians should be aware of increased construction vehicle movement. Please expect changes to traffic and pedestrian routes with the assistance of traffic controllers and follow signs and directions.	Ongoing

The latest in pictures



STKB from the corner of Napier St and Victoria Parade




Level 4 Terrace



Level 6 Terrace



Teaching Space

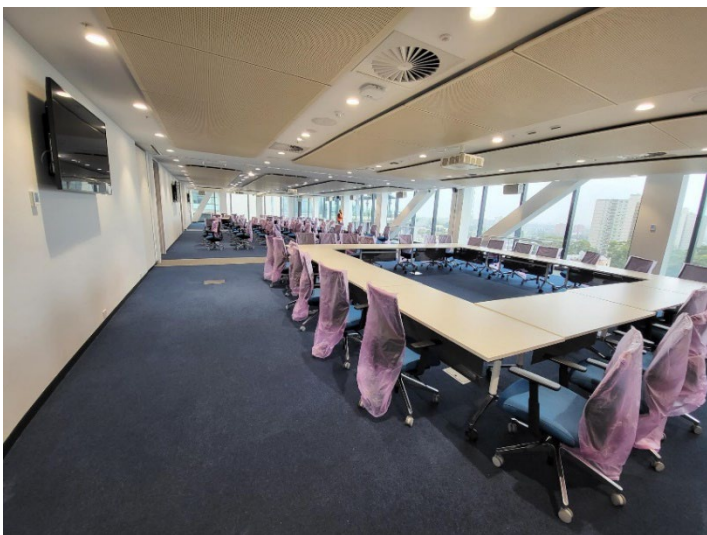

Level 7 Conference Centre



Looking towards the Level 5 Conservatory



Please observe direction and safety signs and follow the instructions of Watpac traffic controllers.

If you wish to provide feedback, contact the team at ACUfeedback@watpac.com.au
